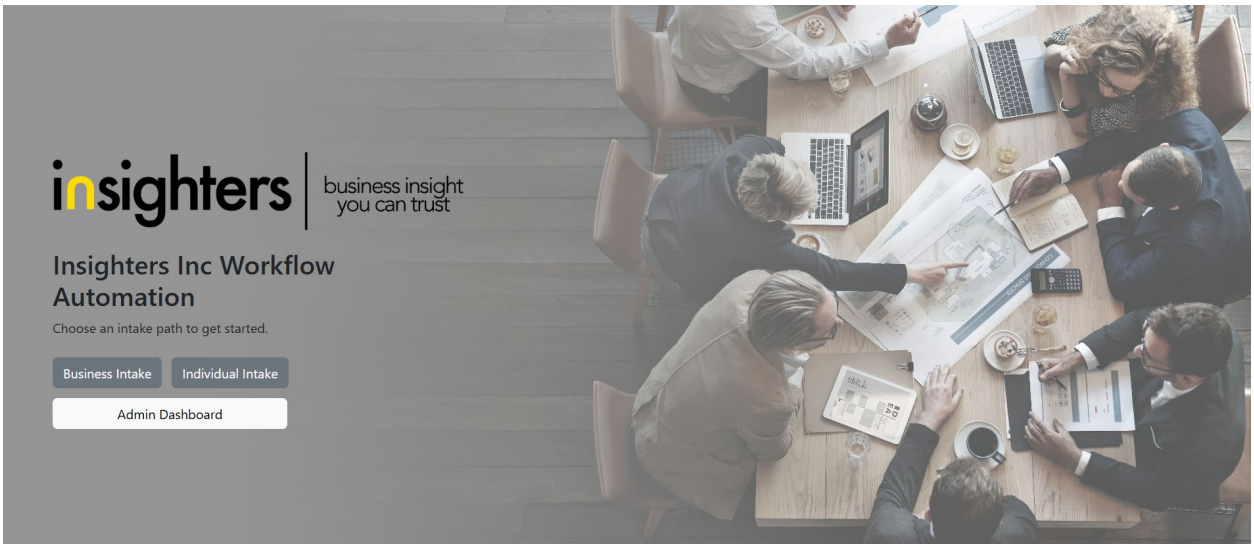

Sprint Planning Document (Sprint 3)
Sprint Goal Backlog (Sprint 3)

March 24 - April 16, 2026

{Tyler Bish, Keegan Doyle, Ayush Singh, Ej Jones}

High-level Project Overview

Project Mission:

- The Insighters Workflow Automation project aims to provide a secure, modernized, and automated client onboarding platform for Insighters Inc. Through this application, the firm can securely collect sensitive tax information, automate document storage, and trigger operational workflows without manual data entry.

Problems We Are Solving:

- There is currently a heavy administrative burden on staff to manually process physical or emailed PDF intake forms.
- Client onboarding tasks (like creating secure folders and notifying the team) are currently decentralized and require manual steps across different platforms (ShareFile, Monday.com).
- Handling Highly Sensitive PII (like SSNs and Bank Routing numbers) via email or unencrypted storage poses a significant security liability.
- Adding additional workflows to Monday.com automatically will drastically reduce the time needed spent on manual repetitive tasks.

Project Overview (High-Level Features):

- **Web-Based Intake Forms:**
  - **Temp Login:** Clients can sign into the emailed form link using a generated temp login to prevent duplicate submissions and form spam.
  - **Business Intake Form:** A secure digital form for corporate clients to submit organizational and financial history.
  - **Individual Intake Form:** A secure digital form for personal tax clients to submit demographic, dependent, and income information.
- **Admin Dashboard:**
  - Login protected dashboard for Insighters Inc. Employees to generate temp logins and email form links to prospective clients using Microsoft OAuth and the Graph API
- **PII Handling (Security):**
  - The system will accept highly sensitive data (SSNs) but will never save it to the database. Instead, it will temporarily hold the data in memory to generate a completed PDF form.
- **Workflow Integrations:**
  - **Microsoft Graph API:** Utilize the Microsoft Graph API to send emails from Insighters to a prospective client with a link to fill out an intake form. The Graph

API will email Insighters after the successful completion of an intake form by a client.
    - **Monday.com Integration**: Automatically ping the firm's Monday.com board using GraphQL when a new client form is submitted and generate a new client workflow.
    - **PDF Monday.com Integration**: Upload the completed PDF to a secure Monday.com board associated with the new client.

- ## Secure Infrastructure:
    - **Google Cloud Platform (GCP):** Host the application via Cloud Run, utilize Google Secret Manager to protect all API keys and database credentials, and use Cloud SQL to host the database.
    - **Docker:** Containerize the application and database for consistent local development and production deployment.

Sprint 3 Planning

Sprint 3 Goals:

1. **Finalize Public Cloud Deployment**
2. **Setup Production Microsoft OAuth Authentication**
3. **Enhance Cloud Security and Penetration Testing**
4. **Finalize PDF Generation and Data Conversion**
5. **Expand Monday.com Automations**
6. **Implement Confirmation Workflows**
7. **Execute Project Handoff and Final Demo**
8. **Finalize Project Website**

Sprint 3 Deliverables:

- **Finalize Public Cloud Deployment:**
  - **Assigned:** {Keegan Doyle}
  - Transition the environment from the private cloud staging area to the final, live public Google Cloud Platform (GCP) deployment.
  - Verify that the Cloud Build pipeline correctly triggers and deploys to the public environment upon merges to the main branch.
  - Make sure all environment variables and Secret Manager configurations are properly mapped to the production Cloud Run instances.
- **Setup Production Microsoft OAuth Authentication:**
  - **Assigned:** {Keegan Doyle}
  - Coordinate with the sponsor's IT to fix the missing Redirect URI login error by configuring the correct production Redirect URIs.
  - Finalize the Microsoft Entra ID App Registration to guarantee a single-tenant security boundary for Insighters Inc. employees.
  - Validate that the django-allauth backend successfully captures offline access tokens for background processing.
- **Enhance Cloud Security and Penetration Testing:**
  - **Assigned:** {Keegan Doyle, Cyber Team, and Tyler Bish}
  - Implement cloud log security protocols to prevent PII from being printed to the GCP Logs Explorer. (Keegan)
  - Conduct comprehensive penetration testing across the application to identify and patch any vulnerabilities. (Cyber Team)
  - Verify that all external API integrations (Monday.com and Microsoft Graph) are securely transmitting data over HTTPS. (Tyler)
- **Finalize PDF Generation and Data Conversion:**

    - **Assigned:** {Ayush Singh}
    - Finalize the backend PDF generation engine to accurately map individual and business form submissions into their respective templates.
    - Apply minor fixes and polish the final PDF outputs.
    - Develop the data conversion and formatting logic required to prepare cleaned database entries for export to Monday.com.
- **Expand Monday.com Automations:**
    - **Assigned:** {Tyler Bish}
    - Push finalized Monday.com board functionality updates, including QOL features requested by the Insighters staff.
    - Develop the GraphQL file upload logic to handle document transmission.
    - Configure the application to automatically push and save the securely generated PDFs directly to the newly updated Monday.com board items.
- **Implement Confirmation Workflows:**
    - **Assigned:** {EJ Jones}
    - Integrate the official Insighters Inc. email system via the Microsoft Graph API.
    - Finalize the communication loop by triggering automated confirmation emails to Insighters after successful form submissions.
    - Ensure the email templates are polished and dynamically populate the correct client information.
- **Automated PDF emailing upon form completion:**
    - **Assigned:** {Keegan Doyle, EJ Jones, Tyler Bish and Ayush Singh}
    - Complete the enterprise documentation suite, including the deployment guide, development guide, testing guide, and user guide.
    - Rehearse the final project demo and polish the presentation slides for the final class review.
    - Conduct the official client handoff meeting with our sponsor to formally transfer GCP billing, IAM ownership, and administrative controls.
- **Update Project Website:**
    - **Assigned:** {Keegan Doyle}
    - Refresh the GitHub Pages project site with new documentation for the Sprint 3 milestones.
    - Upload demo video, documentation, and cyber assessment to the website
